


Construction Update # 11

UPDATE NO.:	011	CONTRACT NO.	21002
DATE ISSUED:	May 19, 2023		
PROJECT NAME:	Talbot Street Construction – Mary St. to Ross St.		

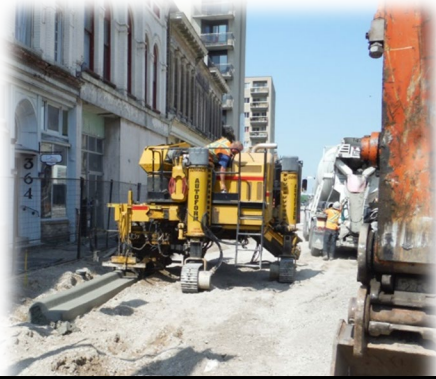

Example of curb machine placing curb in last Phase of Talbot Construction

Happy Friday, I hope you all have a safe and fun long weekend. Next week is a shorter week because of the Holiday, you will see construction pick back up on Tuesday.

Below is a breakdown of the upcoming work for next week and what has been completed so far. As well as some pictures for viewing. For more information, please visit the project webpage at www.stthomas.ca/talbot

Work Scheduled for next week: (Stage 1 only Mary St. to City Hall)

- Finish the last of the Water Service switch overs (Tuesday)
- Sidewalk removals - Front door access may be temporarily interrupted but will be restored quickly (Tuesday)
- Site cleanup and preparation for curb (Tuesday/Wednesday)
- Install Curb (Thursday/Friday) Weather pending

Work completed so far:

(Stage 1 only Mary St. to City Hall)

- Watermain testing completed and passed
- All main line watermain tie ins completed

Road Closures and Access:

- Talbot St. from Mary St to Princess Ave. will be closed to through traffic, please follow the posted detour.
- On street parking within the construction zone is **not** permitted
- Front Door access may be interrupted periodically during construction, advance notification will be provided prior to any disruption

Construction Safety:

- Your safety is very important to us. Please respect the work zone
- Please use caution when using the street or sidewalks near the construction limits
- Maintain a safe distance from any moving equipment, stockpiles or trenches



Example of how the curb will look once completed
