


Construction Update # 13

UPDATE NO.:	013	CONTRACT NO.	21002
DATE ISSUED:	June 02, 2023		
PROJECT NAME:	Talbot Street Construction – Mary St. to Ross St.		

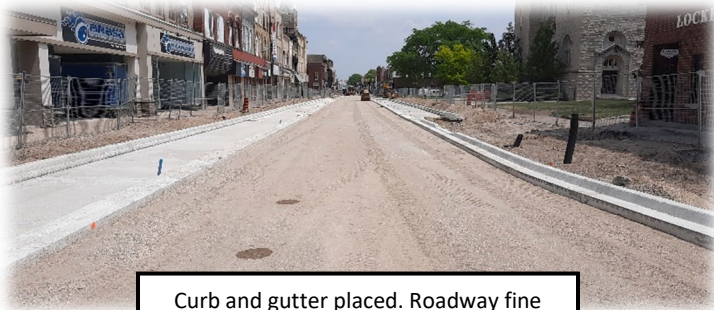

Curb and gutter placed. Roadway fine graded and ready for base asphalt

Good afternoon, I hope everyone has had a good week and is enjoying the nice weather we are having. Another week of construction is completed, and the finishing works are taking shape.

Below is a breakdown of the upcoming work for next week and what has been completed so far, as well as some pictures for viewing. For more information, please visit the project webpage at www.stthomas.ca/talbot

Work Scheduled for Next Week: (Stage 1 only Mary St. to City Hall)

- Placement of base asphalt (Monday/Tuesday)
- Installation of planter boxes/benches
- Removing construction fencing
- Preparation for sidewalk and brick paver stones

Work Completed So Far: (Stage 1 only Mary St. to City Hall)

- Installed curb and gutter
- Poured concrete parking lay-by
- Fine road grading for asphalt placement



Concrete Lay-by ready for brick pavers to be placed.

Road Closures and Access:

- Talbot St. from Mary St to Princess Ave. will be closed to through traffic, please follow the posted detour.
- On street parking within the construction zone is **not** permitted
- Front Door access may be interrupted periodically during construction, advance notification will be provided prior to any disruption

Construction Safety:

- Your safety is very important to us. Please respect the work zone
- Please use caution when using the street or sidewalks near the construction limits
- Maintain a safe distance from any moving equipment, stockpiles or trenches
