

Construction Update # 4

UPDATE NO.:	004	CONTRACT NO.	21002
DATE ISSUED:	April 6, 2023		
PROJECT NAME:	Talbot Street Construction – Mary St. to Ross St.		



Good afternoon, I hope everyone has a safe and fun Easter weekend. The construction crew will be off tomorrow as part of the easter holiday and will be back at it on Monday April 10th.

Below is a breakdown of the upcoming work for next week and what has been completed so far. As well as some pictures for viewing. For more information, please visit the project webpage at www.stthomas.ca/talbot

Work Scheduled for next week: (Stage 1 only Mary St. to City Hall)

The mainline sanitary sewer in stage 1 is almost completed and should be wrapped up next week. They will continue to finish connecting the last few Sanitary services to each building and then will move on to installing the new mainline watermain. All planned water disruptions will be communicated in advance. If your business is water sensitive and you wish to have an after-hour connection, please reach out rpflanzner@stthomas.ca if you haven't done so already.

Work completed so far:

(Stage 1 only Mary St. to City Hall)

- Pulverize asphalt
- Curb removal
- Install Sanitary by-pass pumping
- Mainline Sanitary sewer installed from Mary to Mondamin Street

Road Closures and Access:


- Talbot St. from Mary St to Princess Ave. will be closed to through traffic, please follow the posted detour.
- On street parking within the construction zone is **not** permitted (refer to attached Parking map for downtown parking locations)
- Front Door access may be interrupted periodically during construction, advance notification will be provided prior to any disruption

Construction Safety:

- Your safety is very important to us. Please respect the work zone
- Please use caution when using the street or sidewalks near the construction limits
- Maintain a safe distance from any moving equipment, stockpiles or trenches



Digging to replace sanitary sewer

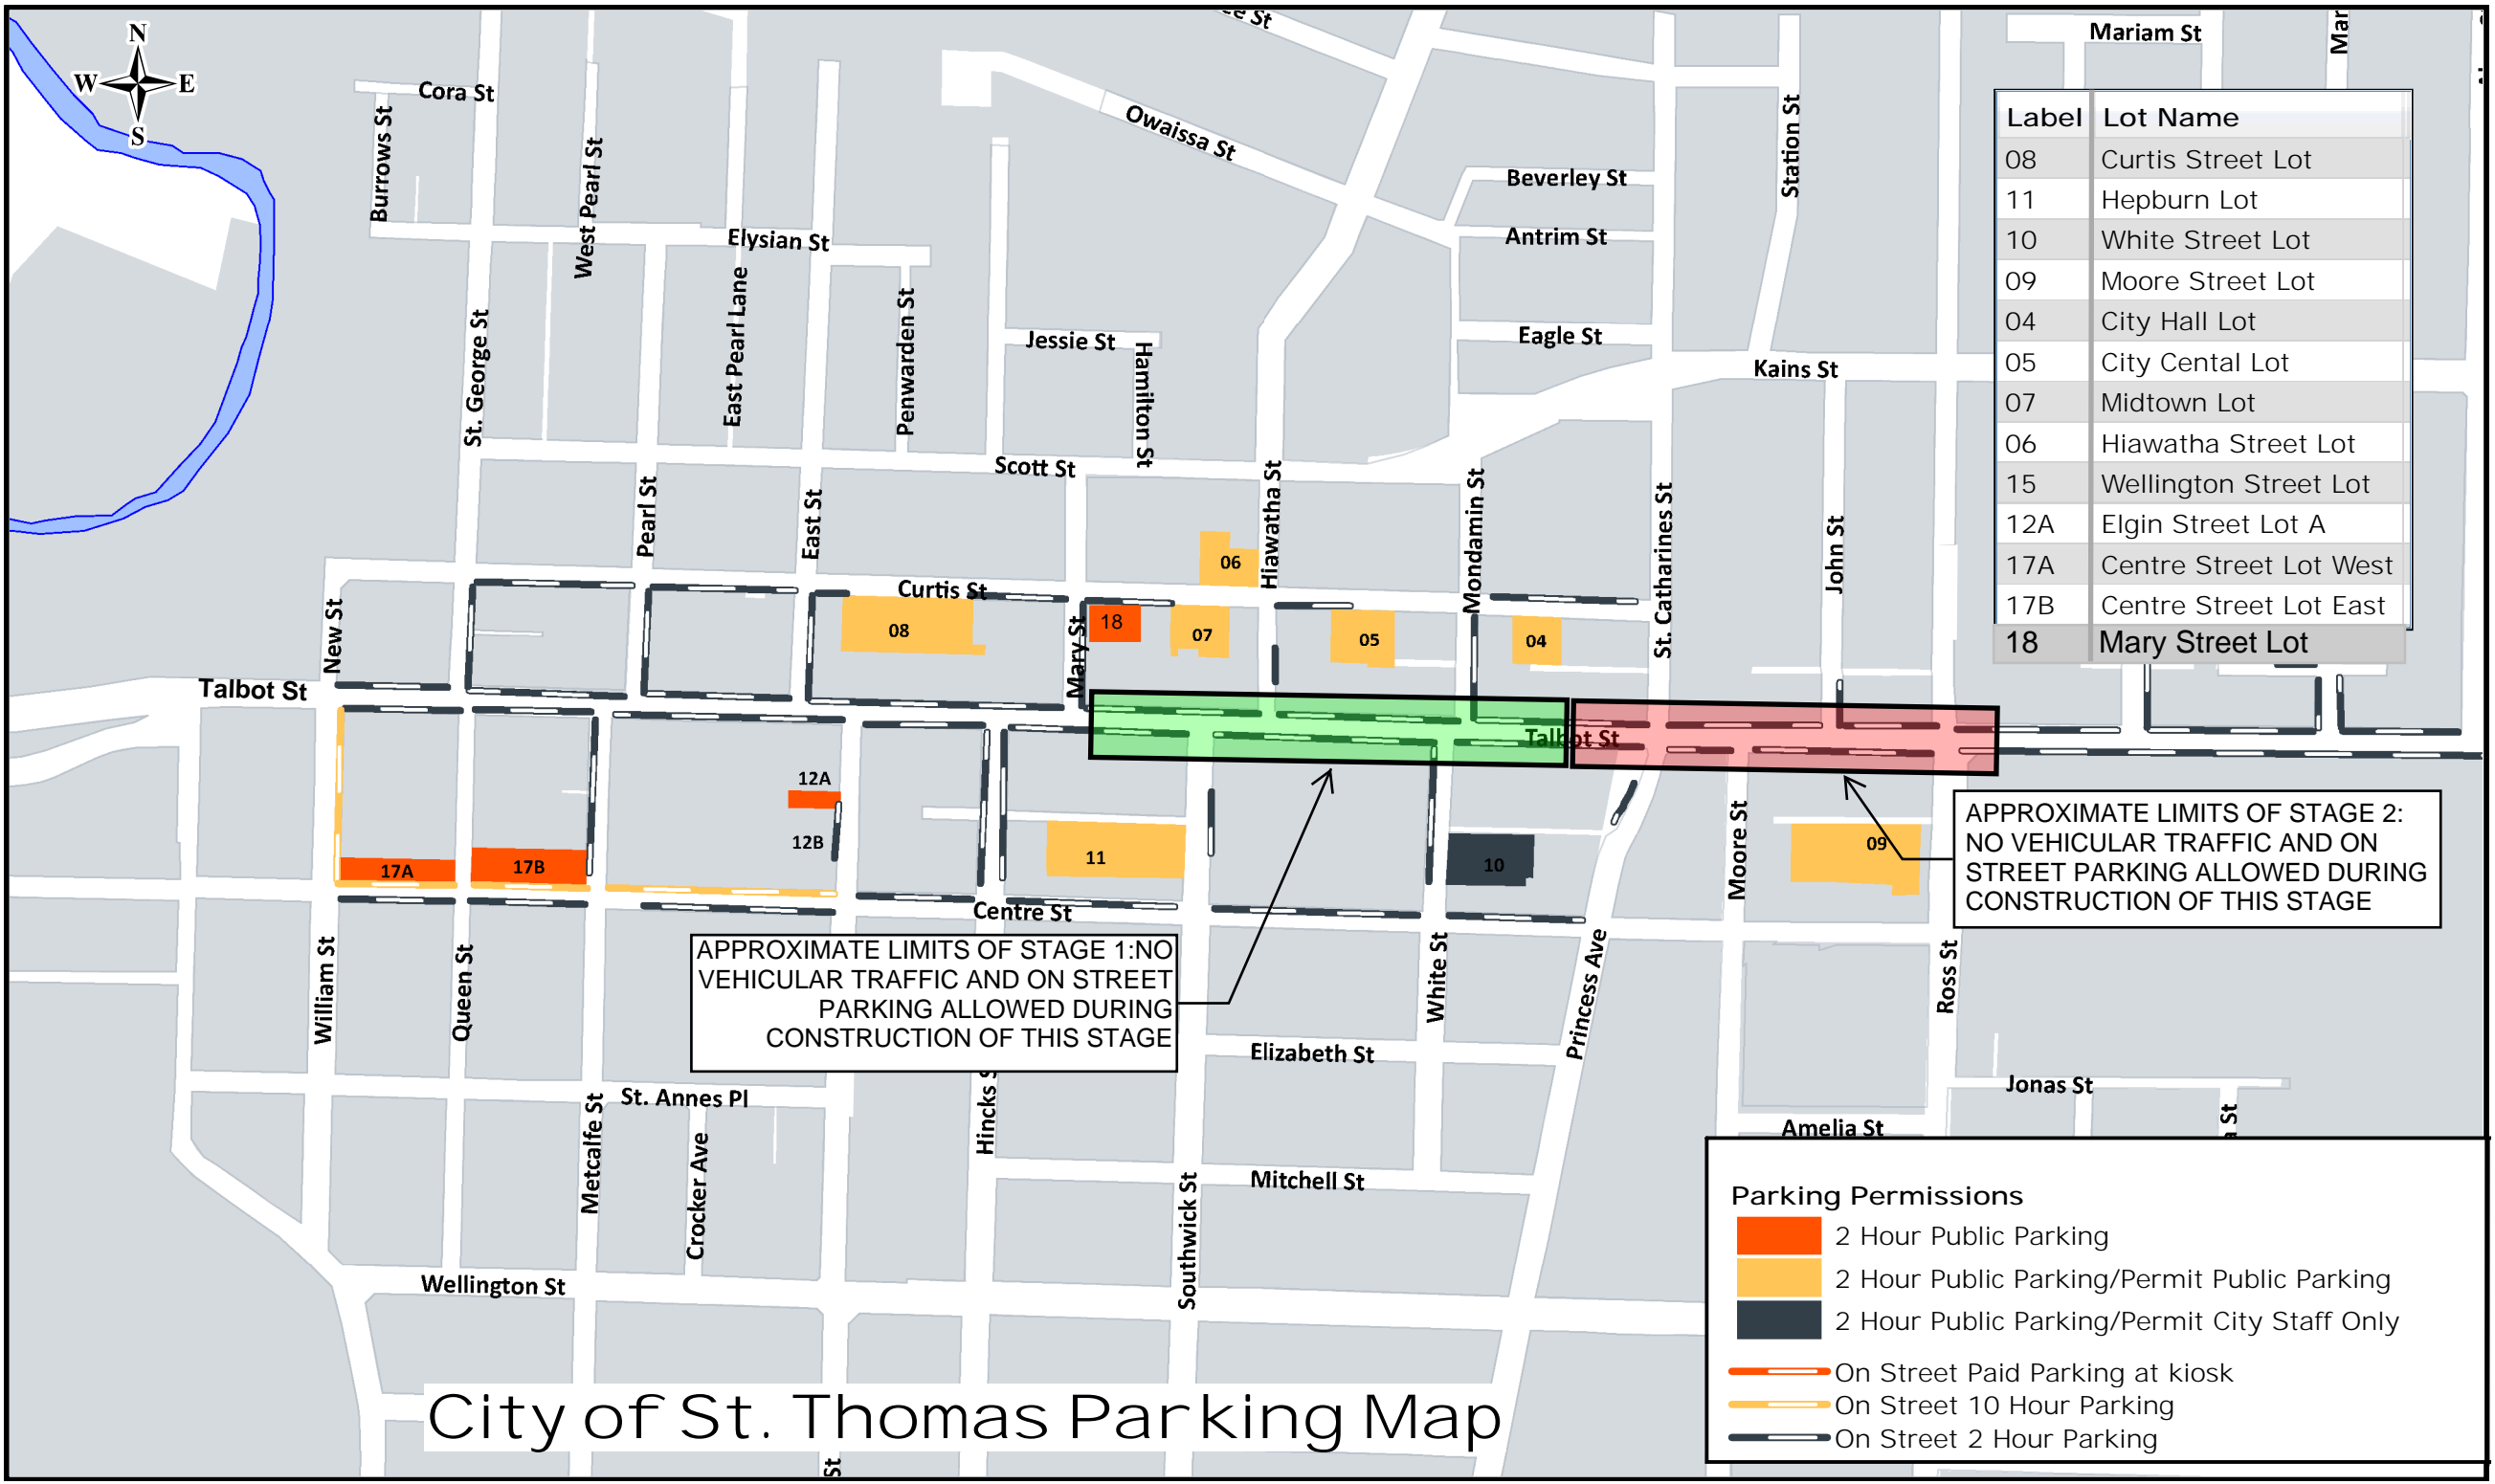

Label	Lot Name
08	Curtis Street Lot
11	Hepburn Lot
10	White Street Lot
09	Moore Street Lot
04	City Hall Lot
05	City Cental Lot
07	Midtown Lot
06	Hiawatha Street Lot
15	Wellington Street Lot
12A	Elgin Street Lot A
17A	Centre Street Lot West
17B	Centre Street Lot East
18	Mary Street Lot

APPROXIMATE LIMITS OF STAGE 1: NO VEHICULAR TRAFFIC AND ON STREET PARKING ALLOWED DURING CONSTRUCTION OF THIS STAGE

APPROXIMATE LIMITS OF STAGE 2: NO VEHICULAR TRAFFIC AND ON STREET PARKING ALLOWED DURING CONSTRUCTION OF THIS STAGE

Parking Permissions

- 2 Hour Public Parking
- 2 Hour Public Parking/Permit Public Parking
- 2 Hour Public Parking/Permit City Staff Only
- On Street Paid Parking at kiosk
- On Street 10 Hour Parking
- On Street 2 Hour Parking

City of St. Thomas Parking Map
